Lab 2: Agile Backlog Creation & Sprint Simulation in Jira

Problem Statement #55 — Book Club Reading Challenge & Discussion Portal

Name : Sateesh

SRN : PES1UG24AM397

---

1. Project Overview

This report documents the conversion of the functional requirements identified in Lab 1 for the Book Club Reading Challenge & Discussion Portal (Problem Statement #55) into an Agile backlog in Jira. The requirements were grouped into three Epics, broken down into User Stories, prioritized, estimated using the Fibonacci scale, and executed across two simulated sprints on a Scrum board. Sprint progress was tracked using Jira's Burndown Chart.

2. Epics

The following Epics were created in Jira, derived from the Lab 1 functional requirements table:

Epic	Description
Epic 1: Reading Progress Management	Enables club members to set and track a personal reading page goal for a selected book (FR-003).
Epic 2: Chapter Discussion & Spoiler Management	Enables members to create and participate in chapter-specific discussion threads, while keeping spoiler-tagged content hidden until explicitly revealed (FR-001, FR-002).
Epic 3: Monthly Book Selection & Voting	Enables members to vote in the active monthly poll and allows the Discussion Lead to create, manage, and close monthly book-selection polls, with duplicate-vote prevention and access control (FR-004, FR-005, NFR-001, NFR-002).


3. User Stories

For each Epic, User Stories were written in the standard "As a / I want / So that" format, prioritized, and assigned story points using Planning Poker and the Fibonacci sequence.


ID	Epic	User Story	Priority	Story Points
1.1	Reading Progress Management	As a club member, I want to set a personal page goal for a book, so that I can commit to a reading target.	High	3
1.2	Reading Progress Management	As a club member, I want to see my current progress toward my reading goal, so that I can stay motivated to keep reading.	High	3
2.1	Chapter Discussion & Spoiler Management	As a club member, I want to create a discussion thread tied to a specific chapter, so that I can talk about that chapter with other members.	High	5

ID	Epic	User Story	Priority	Story Points
2.2	Chapter Discussion & Spoiler Management	As a club member, I want to reply to an existing chapter discussion, so that I can share my thoughts with the group.	High	3
2.3	Chapter Discussion & Spoiler Management	As a club member, I want spoiler-tagged content to stay hidden by default, so that I don't accidentally see plot details from unread chapters.	High	5
2.4	Chapter Discussion & Spoiler Management	As a club member, I want to reveal spoiler content or mark a chapter as read, so that I can view the full discussion once I'm ready.	High	3
3.1	Monthly Book Selection & Voting	As a club member, I want to cast one vote in the active monthly poll, so that I can help the club fairly choose the next book.	High	5
3.2	Monthly Book Selection & Voting	As a Discussion Lead, I want to create, manage, and close a monthly book-selection poll, so that I can run the selection process each month.	Medium	5


4. Jira Backlog Screenshot

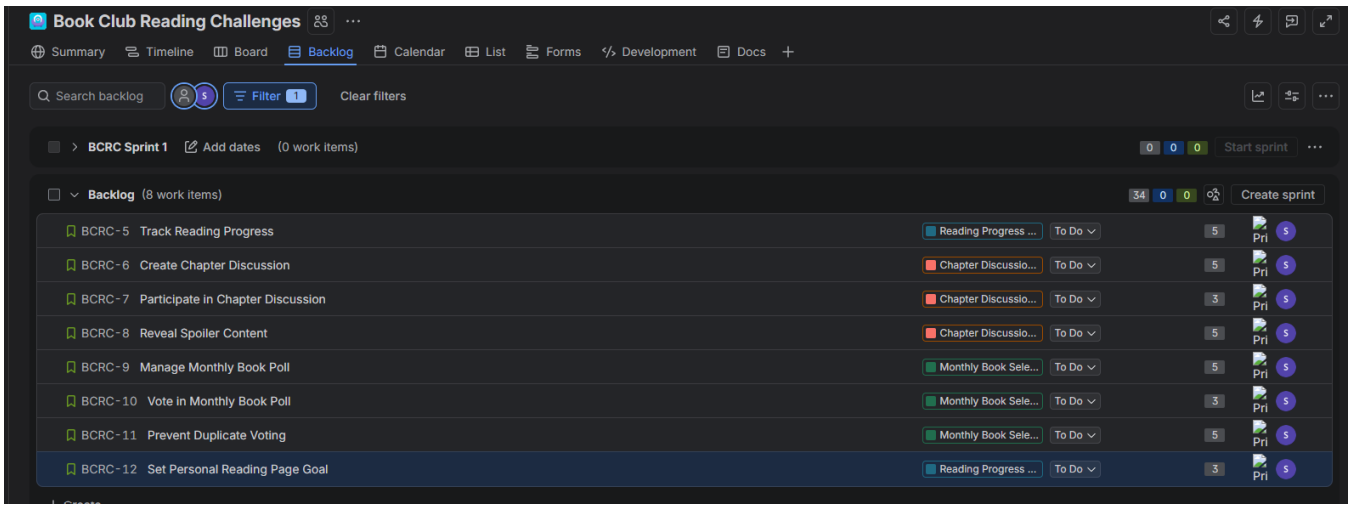


5. Sprint 1 — Active Sprint Board

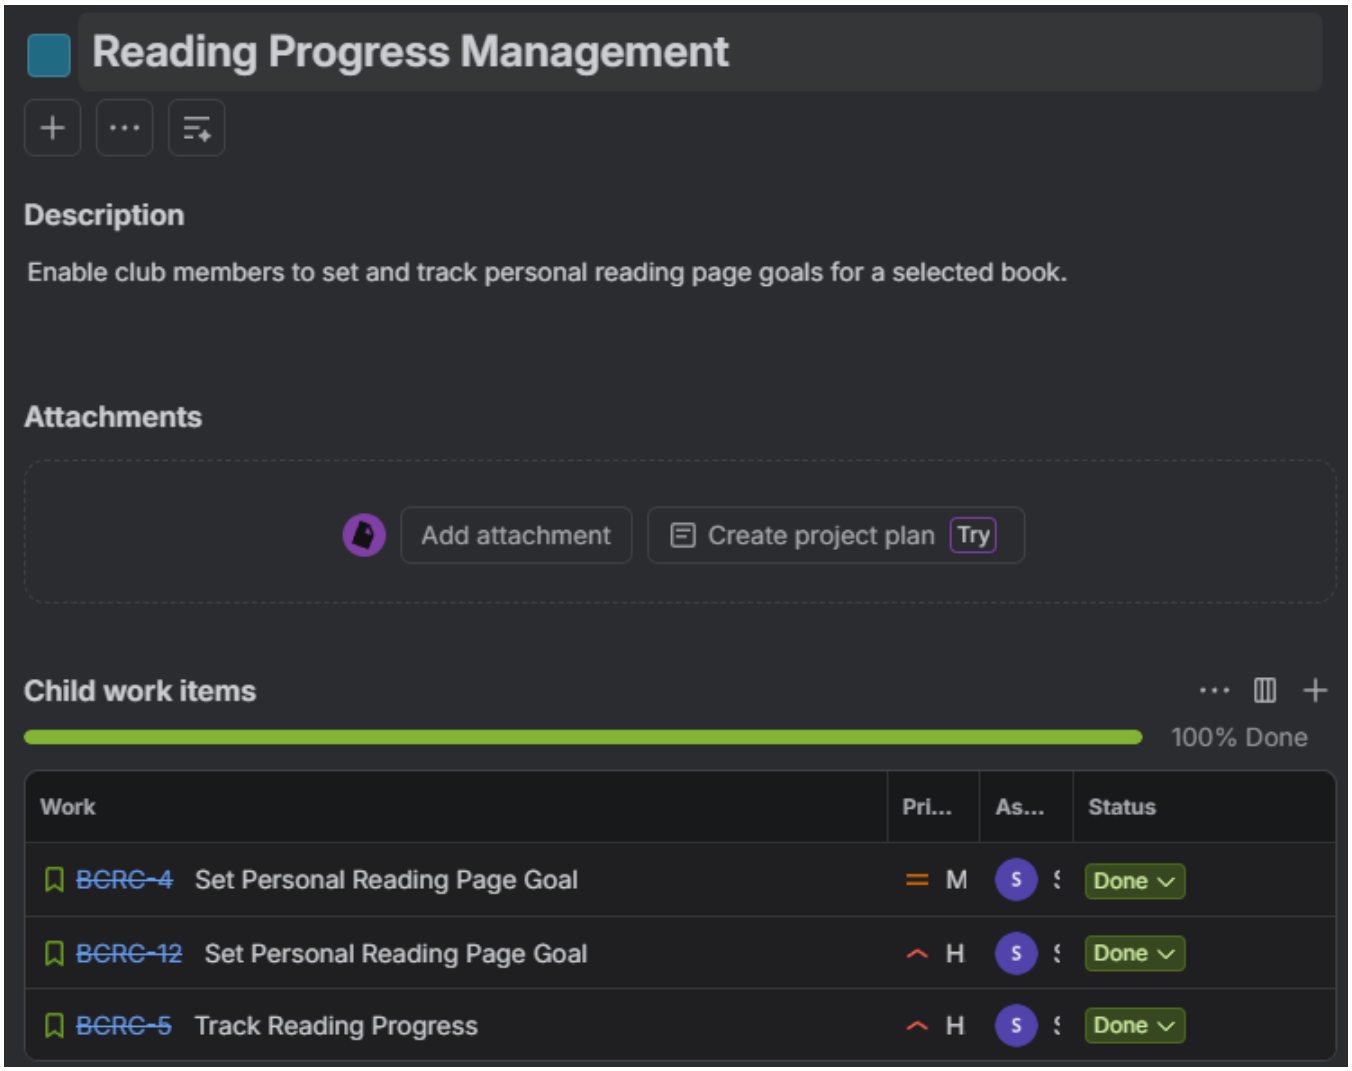

6. Sprint 2 — Active Sprint Board

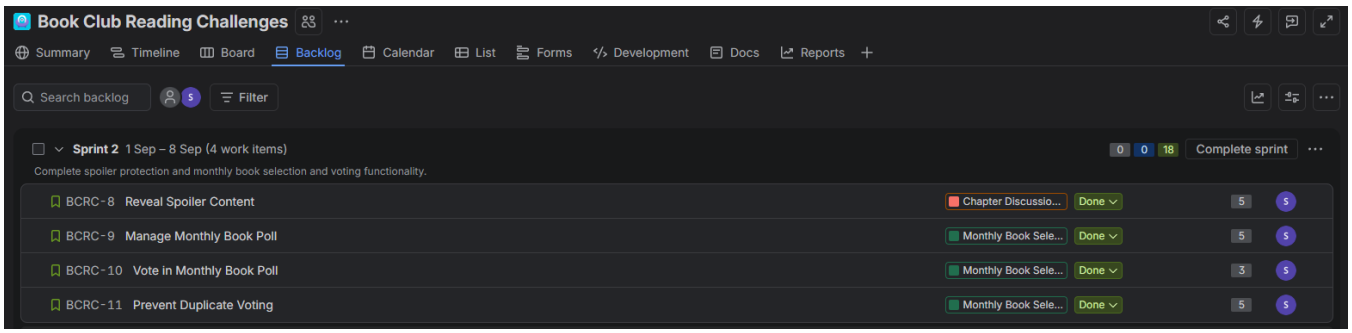

7. Burndown Chart

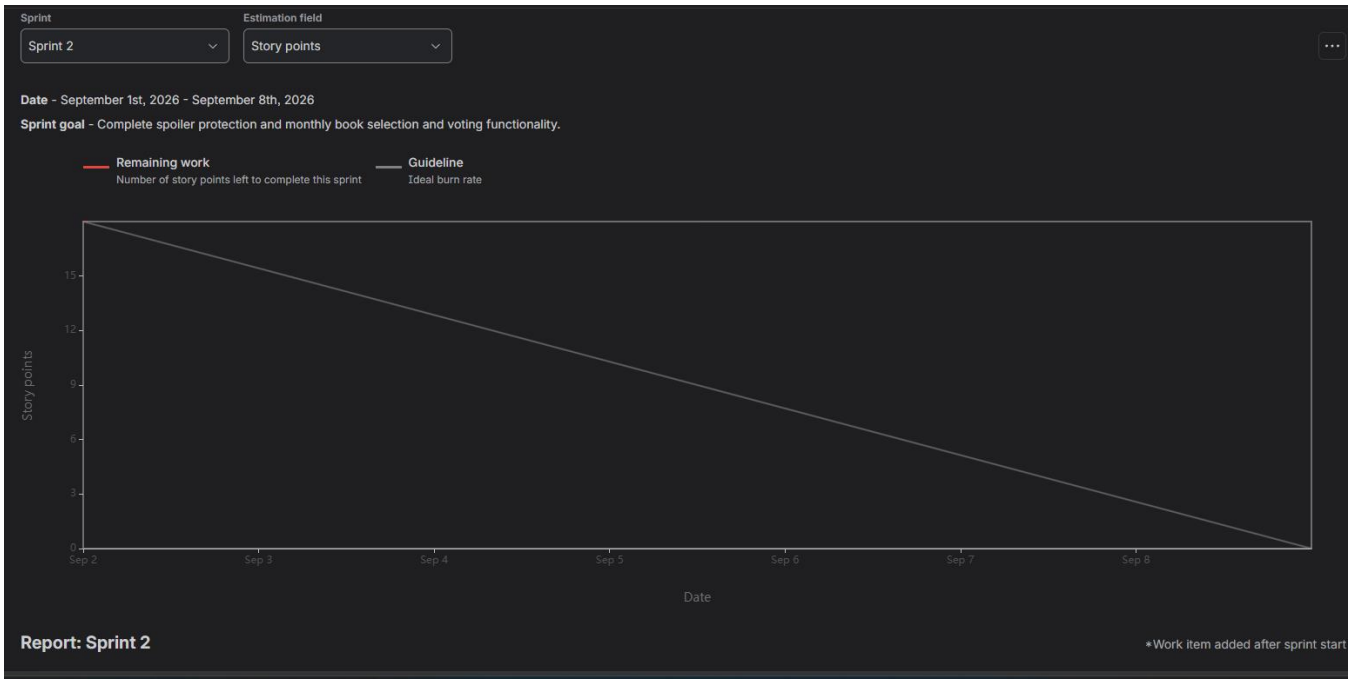

8. Reflection

Q1. Did your estimations reflect the actual effort?

The Fibonacci story-point estimates reasonably reflected the relative effort of the stories. The 3-point stories (e.g., setting a reading goal, tracking progress, replying to a discussion) were completed with less complexity, while the 5-point stories (e.g., spoiler-tag handling, poll voting, discussion thread creation) involved comparatively greater functionality and uncertainty, which matched the higher estimate.

Q2. Was your backlog well-prioritized?

Yes. High-priority items were associated with core member functionality such as reading progress, chapter discussions, spoiler protection, and voting. The monthly poll management functionality was assigned Medium priority because it supports the selection process but is primarily an administrative function handled by the Discussion Lead rather than a day-to-day member action.

Q3. How did your simulated sprint align with your plan?

Sprint 1 contained the reading-progress and core discussion stories, while Sprint 2 contained the spoiler-protection and monthly-voting functionality. The stories were moved from To Do to In Progress and then to Done as planned, reflecting a realistic incremental delivery of the requirements identified in Lab 1.

Q4. What insights did the burndown chart give about your team's capacity?

The burndown chart showed a steady reduction in remaining story points across each sprint, indicating that the planned workload was manageable within the simulated sprint capacity. Where the reduction occurred faster than the guideline, it suggested the sprint commitment may have been conservative; where it tracked closely with the guideline, it indicated accurate estimation and realistic sprint planning.
